


# Project Fact Sheet

## Jones HS (CR Large)

801 S Rio Grande Ave  
Orlando, FL 32805

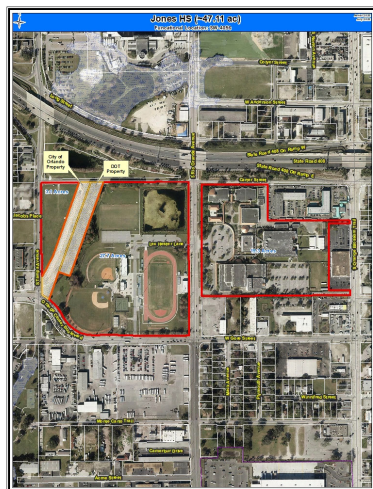

### Project Information:

- **Project Start:** Jun 2022
- **Project Completion:** May 2024
- **Funding Source:** Sales Tax
- **District:** 5
- **Learning Community:** SW
- **Architect/Engineer:** KBJ Architects
- **Contractor:** McCree General Contractors
- **Project Manager:** Daya Taylor
- **Project Budget:** \$6.8 M

### Project Description:

Replacement of approximately 199,000 SF of low sloped modified bitumen roofing at Jones High School with a new single-ply thermoplastic roofing system.

### Project Update:

Long lead time on fasteners. Earliest construction start projected for April 2023, latest start in May. Projected substantial completion is in May 2024.
